PUSD Siesmic Safety Bond
Master Program Schedule for Near-Term Projects

ID	Task Name	Duration	Start	Finish
1				
2	**School Schedule**	**308 days?**	**Fri 6/12/09**	**Wed 8/18/10**
3	Last Staff Day	0 days	Fri 6/12/09	Fri 6/12/09
4	2009 Summer Break	50 days?	Mon 6/15/09	Fri 8/21/09
5	2009-2010 Staff Return	2 days	Mon 8/24/09	Tue 8/25/09
6	2009-2010 School Year	213 days?	Wed 8/26/09	Fri 6/18/10
7	2010 Summer Break	40 days?	Mon 6/21/10	Fri 8/13/10
8	2010-2011 Staff Return	2 days	Mon 8/16/10	Tue 8/17/10
9	2010-2011 School Year Start	0 days	Wed 8/18/10	Wed 8/18/10
10				
11	**Construction Contract Review/Approval**	**63 days?**	**Mon 5/4/09**	**Wed 7/29/09**
12	Staff Review of Contract Form	18 days?	Mon 5/4/09	Wed 5/27/09
13	Board Review of Contract Form	0 days	Wed 5/27/09	Wed 5/27/09
14	**Havens/Driscoll**	**8 days?**	**Mon 6/1/09**	**Wed 6/10/09**
15	DSA Approval	0 days	Mon 6/1/09	Mon 6/1/09
16	GMP Negotiations	8 days?	Mon 6/1/09	Wed 6/10/09
17	Board Approval of GMP	0 days	Wed 6/10/09	Wed 6/10/09
18	**Piedmont High School**	**9 days?**	**Fri 7/17/09**	**Wed 7/29/09**
19	DSA Approval	0 days	Fri 7/17/09	Fri 7/17/09
20	GMP Negotiations	9 days?	Fri 7/17/09	Wed 7/29/09
21	Board Approval of GMP	0 days	Wed 7/29/09	Wed 7/29/09
22	**Beach Portables**	**27 days?**	**Mon 5/4/09**	**Wed 6/10/09**
23	DSA Approval	0 days	Mon 5/4/09	Mon 5/4/09
24	GMP Negotiations	10 days?	Wed 5/27/09	Tue 6/9/09
25	Board Approval of GMP	0 days?	Wed 6/10/09	Wed 6/10/09
26	**Beach Schoolmates Portables**	**13 days**	**Wed 5/27/09**	**Mon 6/15/09**
27	City Approval	0 days	Mon 6/15/09	Mon 6/15/09
28	GMP Negotiations	10 days	Wed 5/27/09	Tue 6/9/09
29	Board Approval of GMP	0 days	Wed 6/10/09	Wed 6/10/09
30				
31	**Construction Schedules**	**307 days?**	**Thu 6/11/09**	**Fri 8/13/10**
32	**Havens/Driscoll**	**307 days?**	**Thu 6/11/09**	**Fri 8/13/10**
33	Abatement	27 days?	Thu 6/11/09	Fri 7/17/09
34	Demolition	27 days?	Thu 6/11/09	Fri 7/17/09
35	Construction	305 days?	Mon 6/15/09	Fri 8/13/10
36	PHS Portables Occupancy	0 days	Mon 8/24/09	Mon 8/24/09
37	Havens/Driscoll Occupancy	0 days	Fri 8/13/10	Fri 8/13/10
38	**Piedmont High School**	**300 days?**	**Mon 6/22/09**	**Fri 8/13/10**
39	Abatement	21 days?	Mon 6/22/09	Mon 7/20/09
40	Demolition	30 days	Mon 6/22/09	Fri 7/31/09
41	Construction	272 days?	Thu 7/30/09	Fri 8/13/10
42	Occupancy	0 days	Fri 8/13/10	Fri 8/13/10
43	**Beach Portables**	**49 days?**	**Mon 6/15/09**	**Thu 8/20/09**
44	Construction	49 days?	Mon 6/15/09	Thu 8/20/09
45	Occupancy	0 days	Thu 8/20/09	Thu 8/20/09
46	**Beach Schoolmates Portables**	**51 days?**	**Thu 6/11/09**	**Thu 8/20/09**
47	Construction	51 days?	Thu 6/11/09	Thu 8/20/09
48	Occupancy	0 days?	Thu 8/20/09	Thu 8/20/09

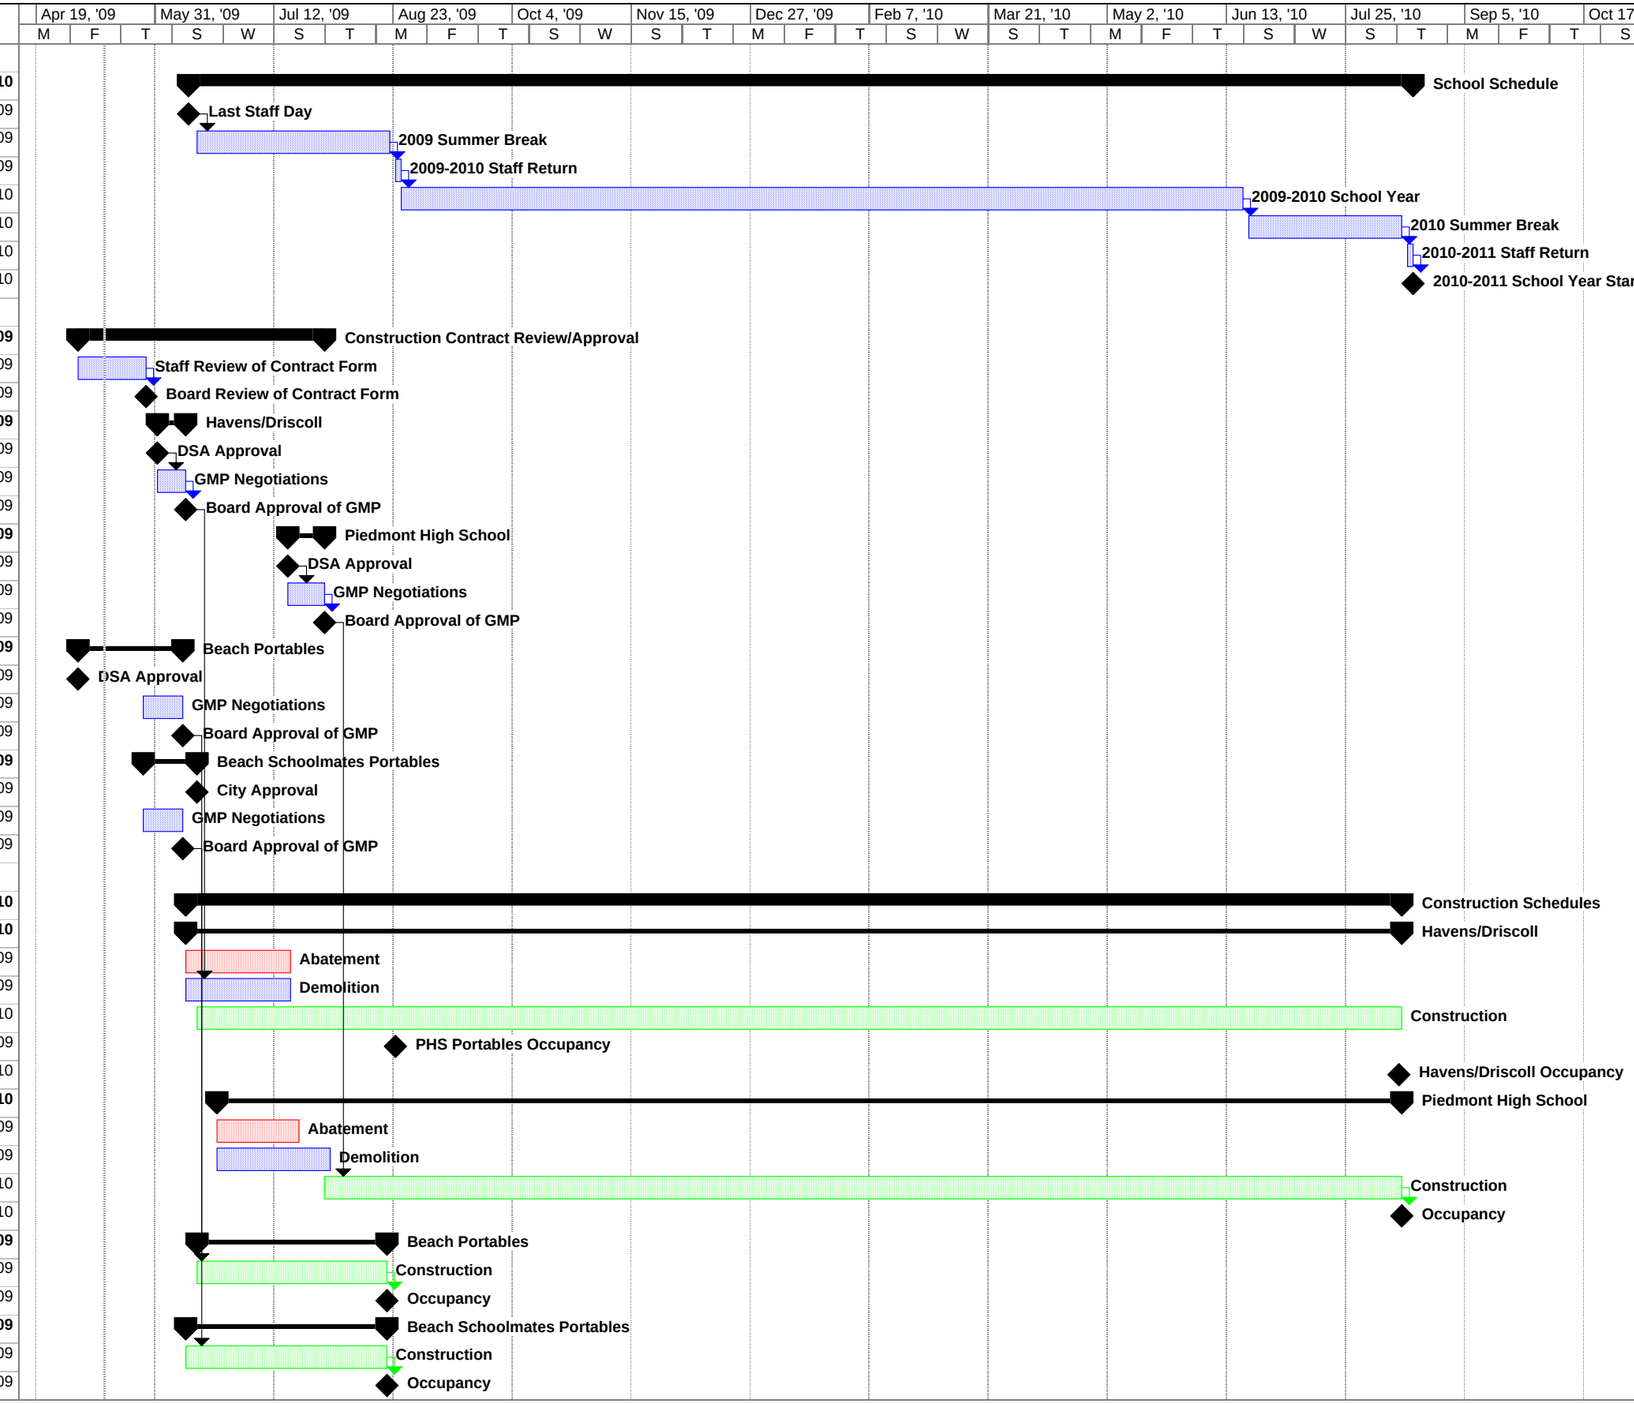

Wed 5/13/09
